
RAPORT Z POMIARU MODULU PV, AGH SOLAR PLANE

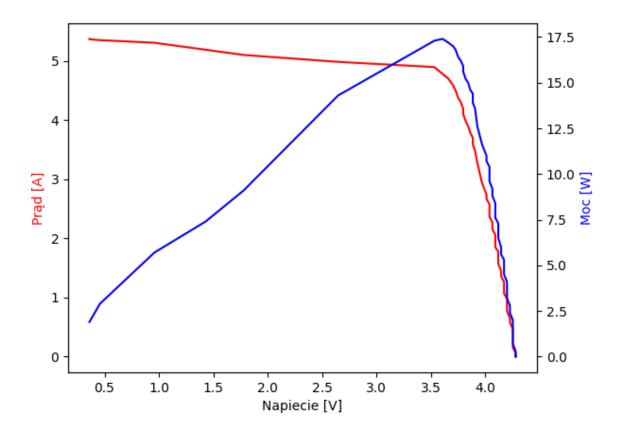

Pmmp = 17.4W Vmmp = 3.607V Immp = 4.779A Voc = 4.278V Isc = 5.374A

Sprawnosc: 18.95%

Czas trwania pomiaru: 9.65s

Warunki pomiaru

Natezenie swiatla = 1000W/m2 Pole ogniwa = 153cm2 liczba ogniw = 6
