
RAPORT Z POMIARU MODULU PV, AGH SOLAR PLANE

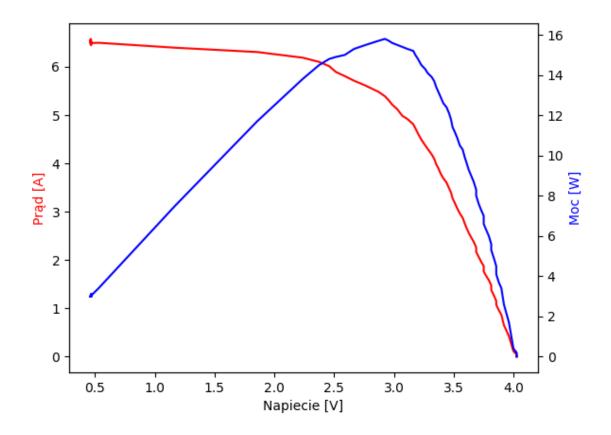

Pmmp = 15.8W Vmmp = 2.926V Immp = 5.389A Voc = 4.028V Isc = 6.563A

Sprawnosc: 17.21%

Czas trwania pomiaru: 9.65s

Warunki pomiaru

Natezenie swiatla = 1000W/m2 Pole ogniwa = 153cm2 liczba ogniw = 6
